

**Original/Duplicate/Triplicate
CONTRACT CERTIFICATE**

SBR-10/30/4
Date.....2018 *18*

No. **First & Final Bill**

(For Other Works)

Division: **BBMP, Byataranyanapura**

Sub-Division: **BBMP, Vidyaranyapura**

Bill Received No.

Dated

Divisional

Cash Book Voucher No..... Dated.....

Sub Divisional

Work Code: 011-18-000008

Schedule Docket No.

Head of Account: **P-1878**

Est.Cost: 25.00 Lakhs D.R.No. :

Name of Work (as per sanctioned estimate: **Improvements to Roads, drains and other works Singapura**

Cross Road and Surrounding area in Ward No. 11(Kuvempunagara)..

Name of Contractor and Full Address: **Executive engineer, Karnataka Rural Infrastructure Development Limited, # 280, 59th Cross Road, 17th 'C' Main Road, 3rd 'Y' Block, Rajajainagara, Bangalore - 10.**

Reference to Agreement No. **EE/BTP/BBMP/KRIDL/WO/121/2017-18**

Dated: 20.03.2018

Certified that the measurements were taken by me on *23.4.2018* and recorded of Pages 424528 to 424536

of measurement Book No. **4246/2017-18** and that the work is satisfactorily executed.

**Assistant Executive Engineer
Byataranyanapura Sub-division
KRIDL, BBMP, Bangalore**

Certified that the measurement were taken by me on and found correct. The work is satisfactorily executed.

Officer-in-charge of work

Certified that the quantities of materials shown in column 3 of Account have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of and imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

II Memorandum of Payment

**Assistant Sub-Division Officer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97**

1) Total value of work done or supplies made as per account within	
2) Deduct amount to be held in reserve being percent Rs.....	
3) " " Balance	
4) Deduct Payment:	
a. Amount of previous payment as in the Office Cash Book Voucher	
No.....Dated.....S.D. No.....	<i>For 1st. Amount</i>
adjusted towards cash advance recovery of	<i>24.99,059-00</i>
b. Payments } cost store or other material supplied.	<i>IT- 44981-00</i>
Now made } recovery of amount creditable to this/other work	<i>CU- 24991-00</i>
} Amount paid on this bill Cheque / Cash.	<i>CBF- 2499-00</i>
5) Balance being unpaid value of work done held in reserve.	<i>LR- 32738-00</i>
6) Deduct cash advance made on the Office cash Book Voucher No.....	<i>FSD- 124953-00</i>
dated.....less adjustments.	
7) Net amount due to or from Contractor	un
adjustments items.	<i>Adju: 2.30,162-00</i>
8) Advance to Contractor for materials brought to site (as detailed) within.	<i>Chaque: 22,68,897-00</i>
9) Value of Government materials supplied.	
Total amount adjusted	

Received Rs..... (in words).....

by cash and by adjustment of Payment as per memorandum

(in final settlement of all demands)

(For use in the Office)

Witness

1.

Assistant Executive Engineer

Byataranyanapura Sub-division

KRIDL, BBMP, Bangalore

Cash Rs.....

Dated.....


Initials of Officer making payment

230162-00
2268897-00
Rs. Twenty two Lakhs Eight thousand eight hundred and ninety seven only
Hand of m... ..
Executive Engineer

Sl. No.		Unit
1	Excavation for road, drains and similar works KSRRB 300-1. Earthwork excavation by manual means in ordinary soil involving an average horizontal throw upto 2 meters and an average lift upto 0.5 m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods etc complete as per specifications and directions of engineer in charge of the work	Cum
2	Removing and refixing stone slabs of drains and pointing in CM (1:3) etc complete as per specifications and directions of engineer in charge of the work	Sqm
3	Providing granite slabs of selected quality roughly dressed havinf a size of 7.5 cms thick and fixed in cement mortar (1:6) including fixing curing etc complete as per specifications and directions of engineer in charge of the work	Sqm
4	Providing and Filling in foundation with granite / trap broken metal 100mm. and down size, with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all lead and lift. etc complete as per specifications and directions of engineer in charge of the work	Cum
5	Providing and laying in position plain cement concrete of mix 1:4:8 with OPC cement @ 180kgs, with 40mm and down size graded granite metal coarse aggregates @0.85cum and fine aggregates @ 0.57cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation , including cost of all materials, labour, HOM of machinery, curing etc complete as per specifications and directions of engineer in charge of the work	Cum
6	Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200 mm having block density not less than 1800 kg/m ³ and having a minimum average compressive strength 4.00 N/mm ² confirming to IS 2185 (Part) : 2005 and constructed with CM 1:4 , as per IS 2572:2005 including cost of all materials, labour charegs, scaffolding, curing etc complete as per specifications and directions of engineer in charge of the work	Sqm
7	Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregtes @ 0.459cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills , ncluding cost of all materials, labour, HOM of machinery, curing etc complete as per specifications and directions of engineer in charge of the work	Cum
8	Providing precast slab of 100 mm thick including cost of all materials, labour, curing, transportation, loading unloading, etc., complete as per the direction of engineer in charge.	Sqm
	Total	
	Add 10% Service charge to KRIDL	
	Add 1% Labour Cess	
	Grand Total	

CERTIFICATE

1. Certified that the above work done satisfactory and no materials issued from departmentally.

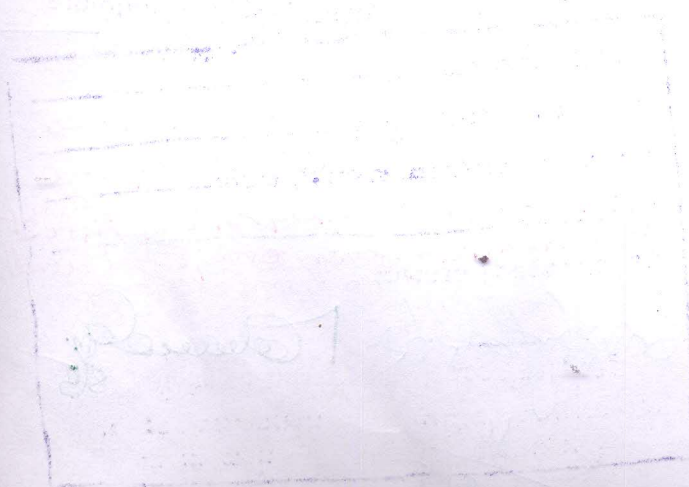

Unit	Previous Measurement		Present Measurement			Total Upto Date		Remarks
	Qty.	Cost	Qty.	Rate Rs. P.	Amount	Qty	Cost	
Cum	-	-	62.64	199.36	12488.00	62.64	12488.00	
Sqm	-	-	626.40	80.56	50463.00	626.40	50463.00	
Sqm	-	-	438.48	665.68	291887.00	438.48	291887.00	
Cum	-	-	62.64	2240.84	140366.00	62.64	140366.00	
Cum	-	-	41.76	5159.02	215441.00	41.76	215441.00	
Sqm	-	-	556.80	993.22	553025.00	556.80	553025.00	
Cum	-	-	39.44	5767.46	227469.00	39.44	227469.00	
Sqm	-	-	417.60	1820.56	760266.00	417.60	760266.00	
					2251405.00		2251405.00	
					225140.50		225140.50	
					22514.05		22514.05	
					2499059.55		2499059.55	

[Handwritten signature in blue ink]

[Handwritten signature in green ink]

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97
